



TAJIKISTAN

PROGRESS ON IMPLEMENTATION OF EXTENSION REQUEST IN ACCORDANCE WITH ARTICLE 5 OF THE CONVENTION

Meetings of the Standing Committees

Geneva, 20-24 June 2011




CONTENT

- 1. Introduction**
- 2. Available capacity in 2011**
- 3. Status of work to be conducted**
- 4. Status of work conducted**
- 5. Contaminated areas as of June 2011**
- 6. Financial support in 2011**
- 7. Operational plans for 2011**
- 8. Other issues**

Mined areas & accident locations in Tajikistan



- Mine accidents: Number of victims
 - 1
 - 2 - 4
 - 5 and more
 - No data
- Demining accidents: Distance from town
 - < 0.5 km
 - 0.5 km to 5 km
 - > 5 km
- Actual Location
- Missing direction or distance
- Mined areas: Start point
- Tajdistricts_region.shp
 - Direct Rule Districts
 - Khatlon
 - Pamir
 - Sughd

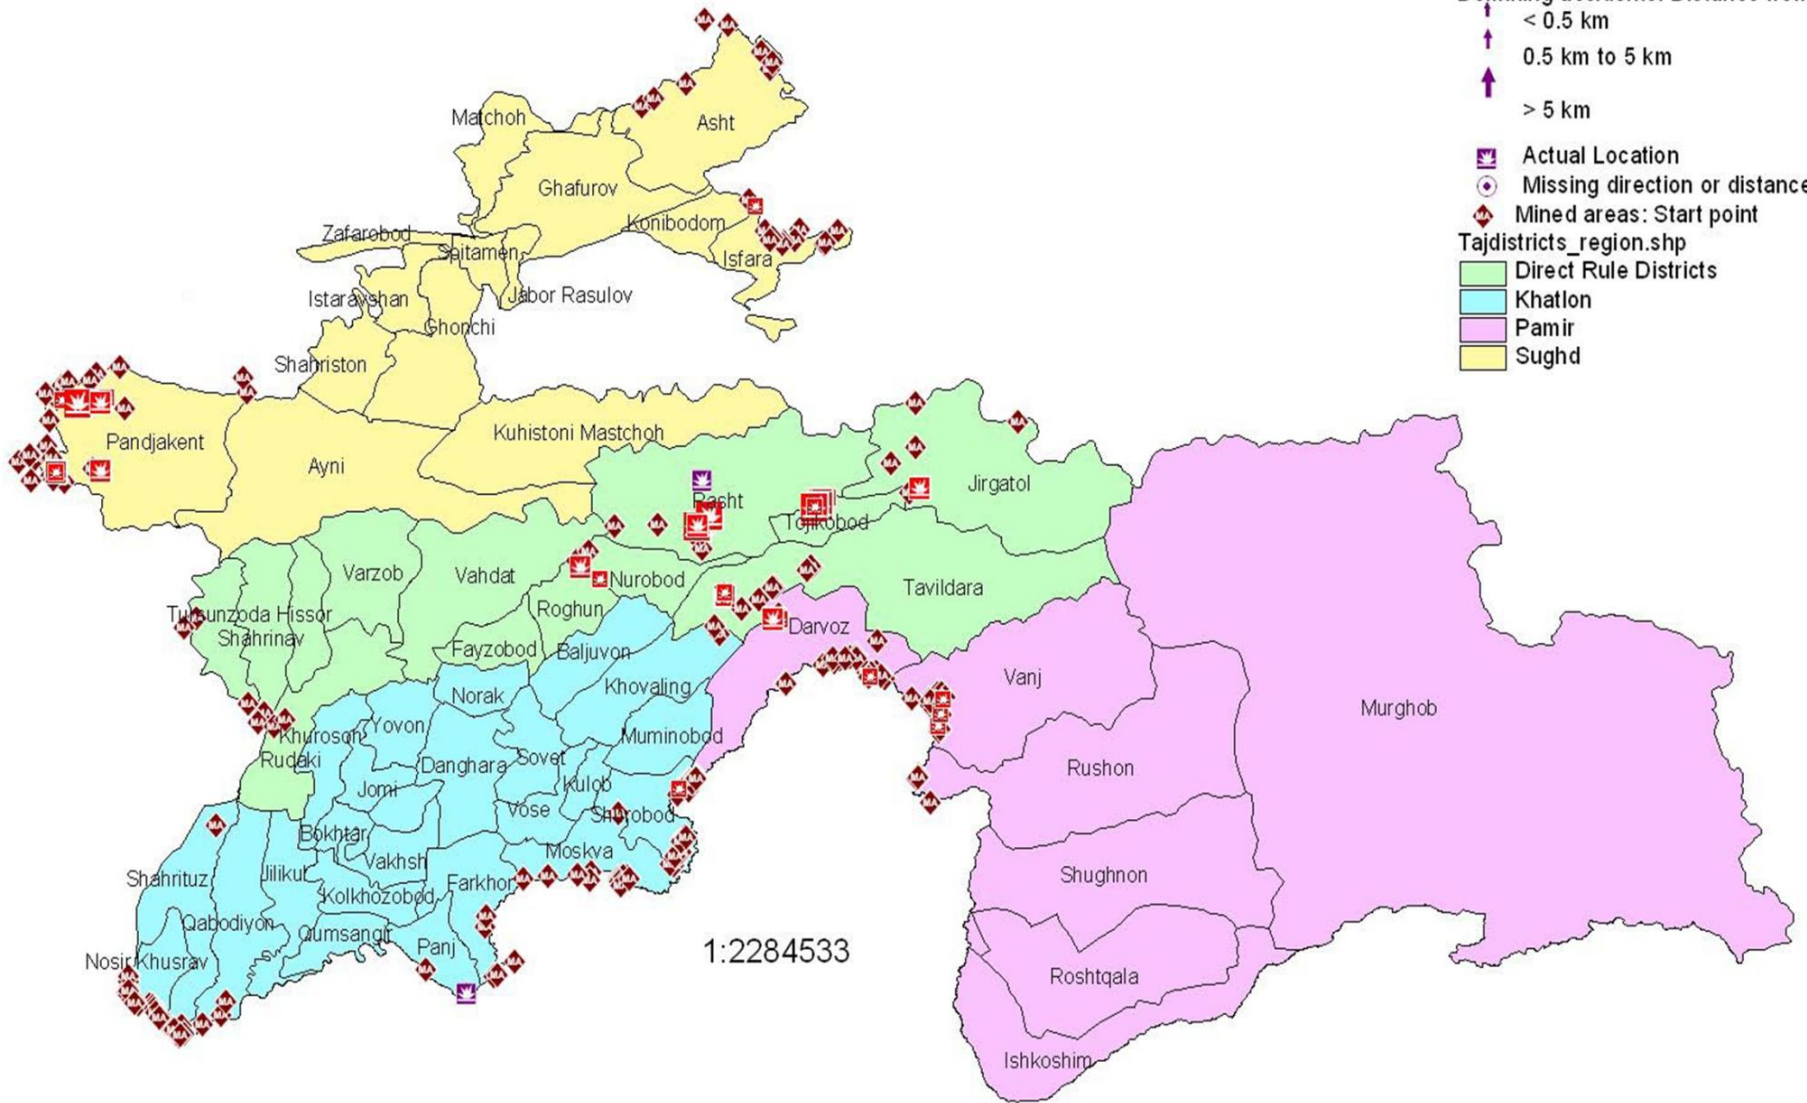

1:2284533



Available capacity in 2010

- **2 FSD Survey Teams**
- **8 FSD Multipurpose Teams**
- **5 MDD Teams (10 dogs) – Managed by FSD**
- **2 FSD mechanical demining teams**
 - **2 MV-4 machines started operations in September 2010**
- **1 MoD mechanical demining team**
 - **1 Mini MineWolf machine started operations in June 2010**
- **4 NPA Multipurpose Teams started operations in November**
 - **Planned to establish of MDC within CoES capacity (8-10 dogs)**

Status of work to be conducted

Assumptions for 2010 in accordance with Work Plan of Extension Request

	Land release by	Number of areas to be cleared or reduced	Size to be cleared or reduced, m ²
Tajik Afghan border	MDM	9	800,000
	MDD	1	400,000
	Manual	2	200,000
Central Region	MDM	2	200,000
	Manual	2	100,000
		16	1,700,000

Status of work conducted

Progress made in 2010

	Land released by	Number of cleared areas	Cleared size, m ²
	MDM/REDUCTION	-	630 000
	MDD	7	441 000
	Manual	8	807 000

Central Region	MDM/REDUCTION	-	-
	Manual	-	-

22	1 878 000
-----------	------------------

Status of work to be conducted

Assumptions for 2011 in accordance with Work Plan of Extension Request

	Land release by	Number of areas to be cleared or reduced	Size to be cleared or reduced, m ²
Tajik Afghan border	MDM	21	700,000
	MDD	7	400,000
	Manual	1	200,000
Central Region	MDM	4	500,000
	Manual	2	100,000
		35	1,900,000

Status of work conducted

Progress made in 2011 by June

	Land released by	Number of cleared areas	Cleared size, m ²
Tajik-Afghan border	MDM/REDUCTION		530 000
	MDD		280 000
	Manual	2	180 000
	Visual		20 000
Central Region	MDM/REDUCTION	-	-
	Manual	-	-
		2	480 000

Contaminated areas as of June 2011

Total size of contaminated and leftover areas:

- Tajik-Afghan Border: 191 areas – 7,2 km²**
- Central region: 26 areas - 2,5 km²**
- Tajik-Uzbek border: 57 areas - unsurveyed**



Financial support in 2011

Canada

OSCE

France

UNDP

Germany

ICRC

Japan

Norway

USA



Operational plans for 2011

- Conduct resurvey in Central region;
- Clearance of not less than 300,000 m² of the land manually;
- Clearance not less than 400,000 m² of the land by the MDDs;
- Clearance not less than 1,200,000 m² of the land by the MDM;



Other issues

- TMAC Nationalization
- Contribution of Government
- MRE activity
- Tajik – Uzbek border



Thank you for your attention
