


بِسْمِ اللَّهِ الرَّحْمَنِ الرَّحِيمِ





Yemen Mine Action Program



Identifying mined areas

Level one impact survey
1999-2000

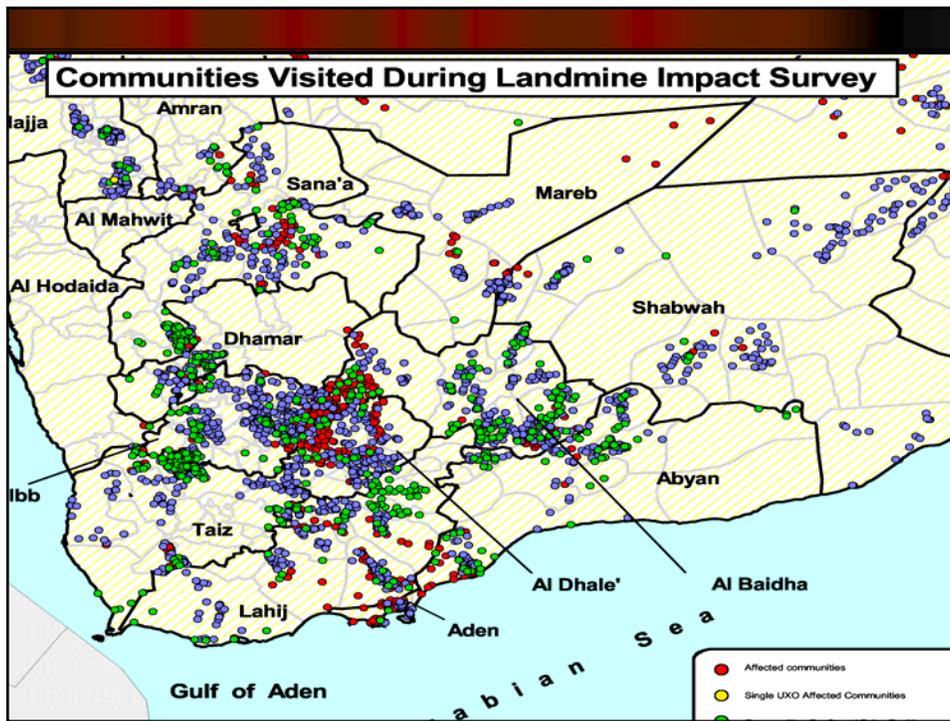

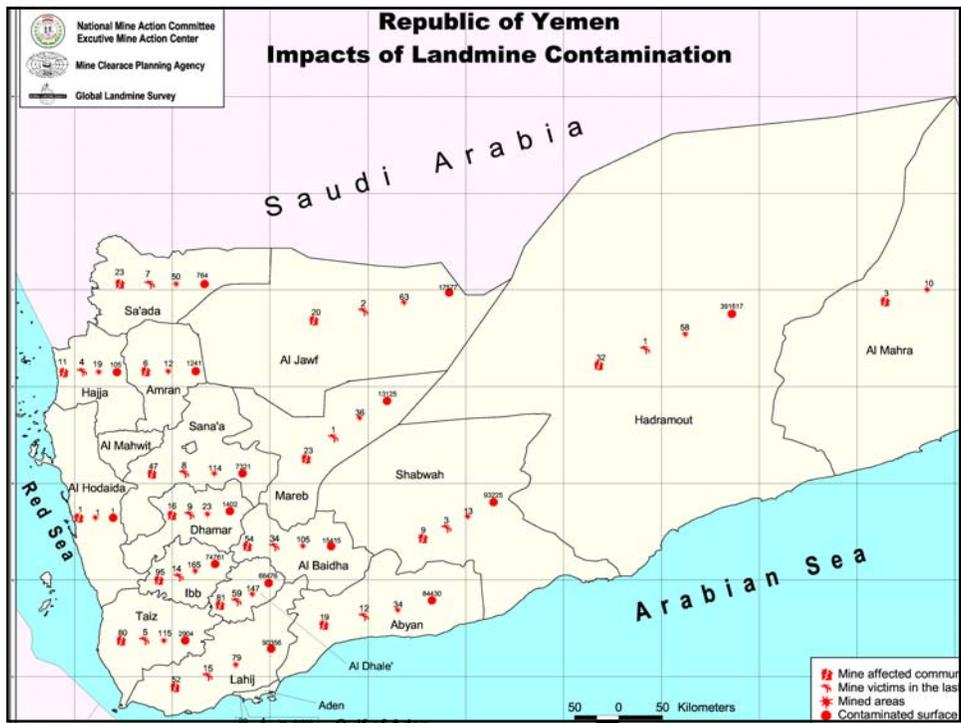


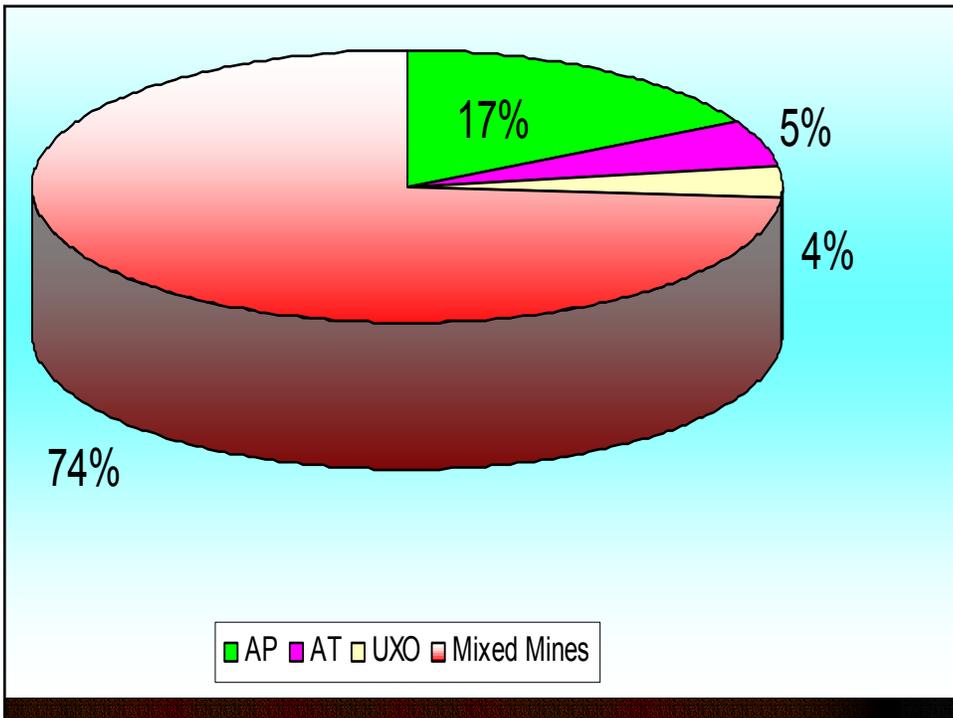


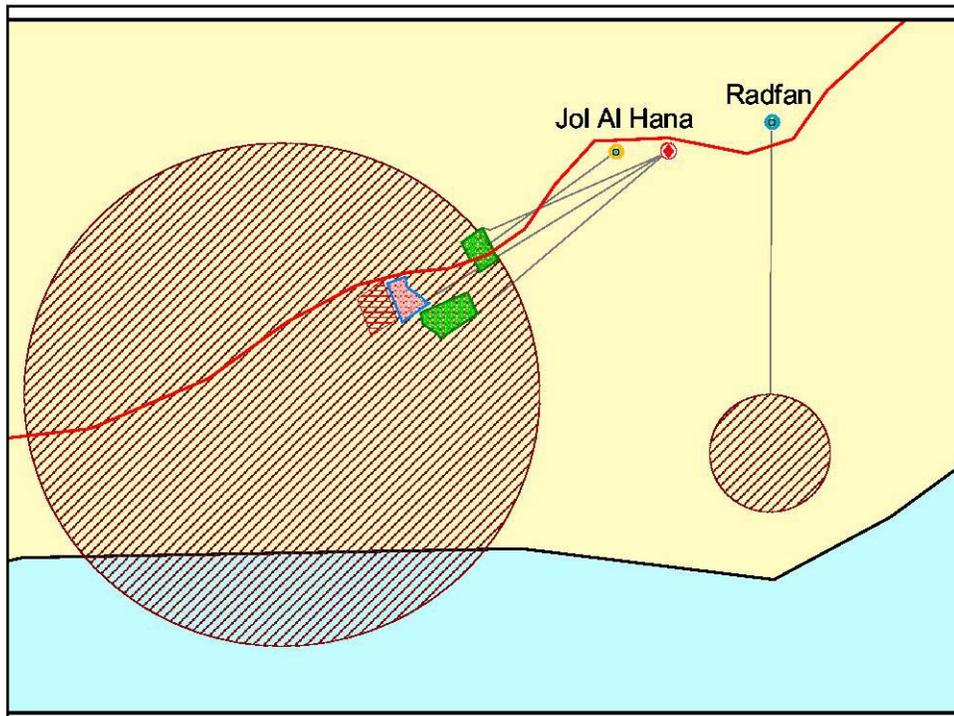
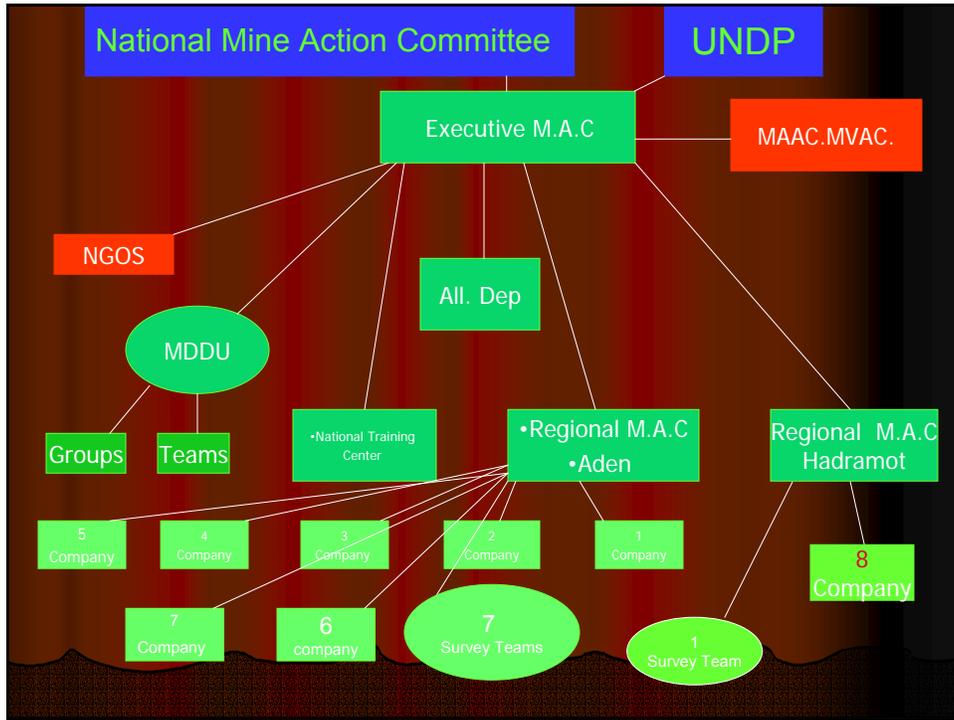


One more area been funded
during Level two survey

Developing National Plan

- The first strategic plan 2000-2004 developed in 2000.
- It has been extended to 2009
- Envision to put an end to suffering of people in Yemen
- All high, medium and 27% of most critical low impacted areas will be finished by March 2009
- All survivors medically support/rehabilitated and reintegrated into the communities.

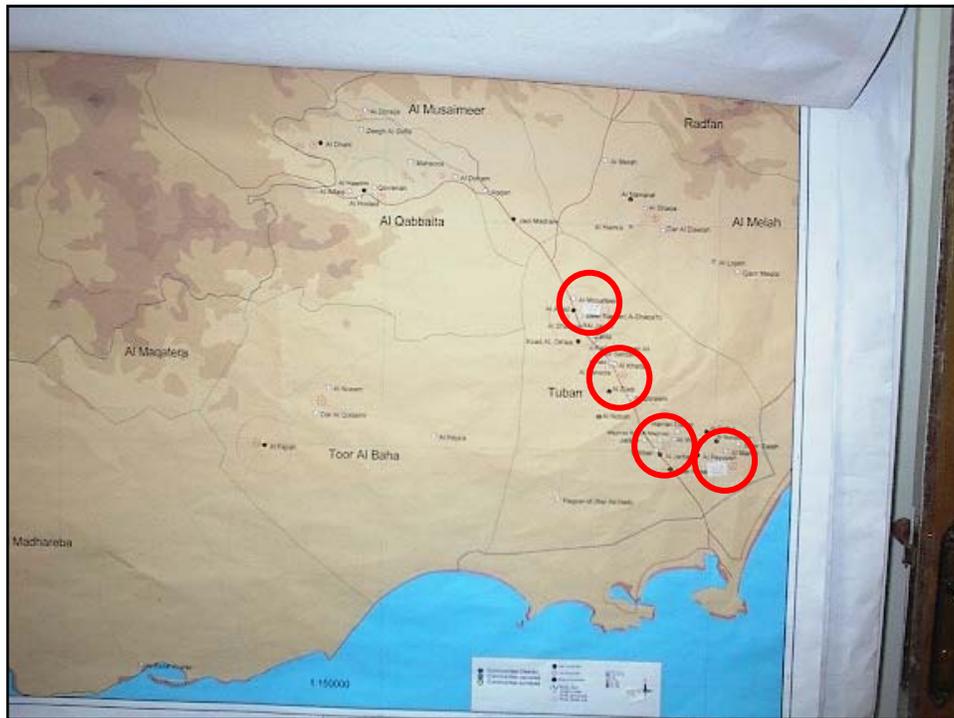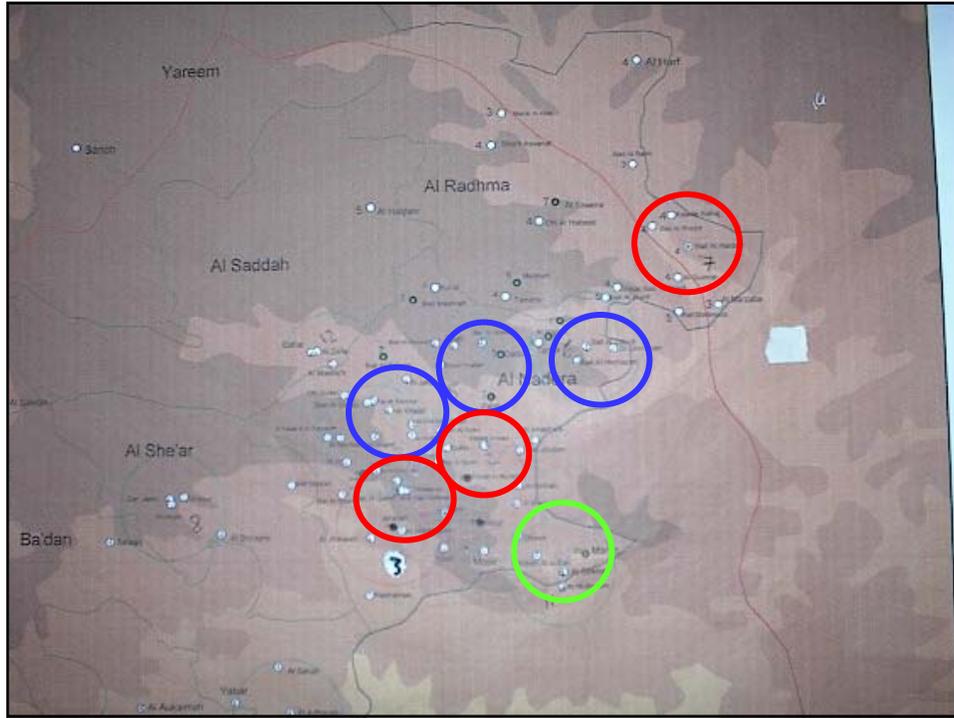

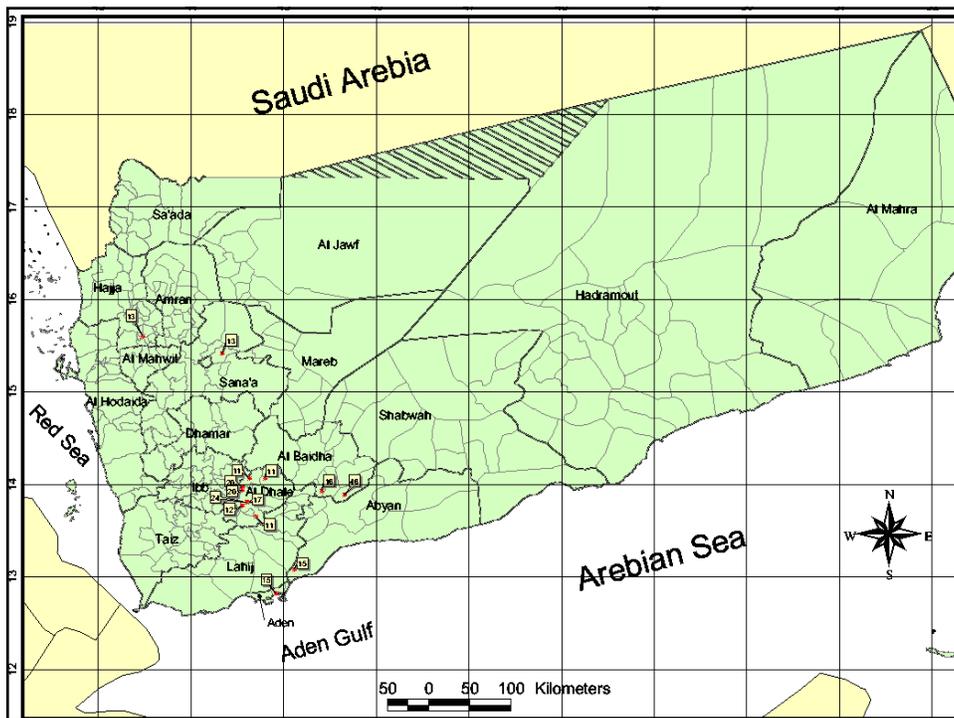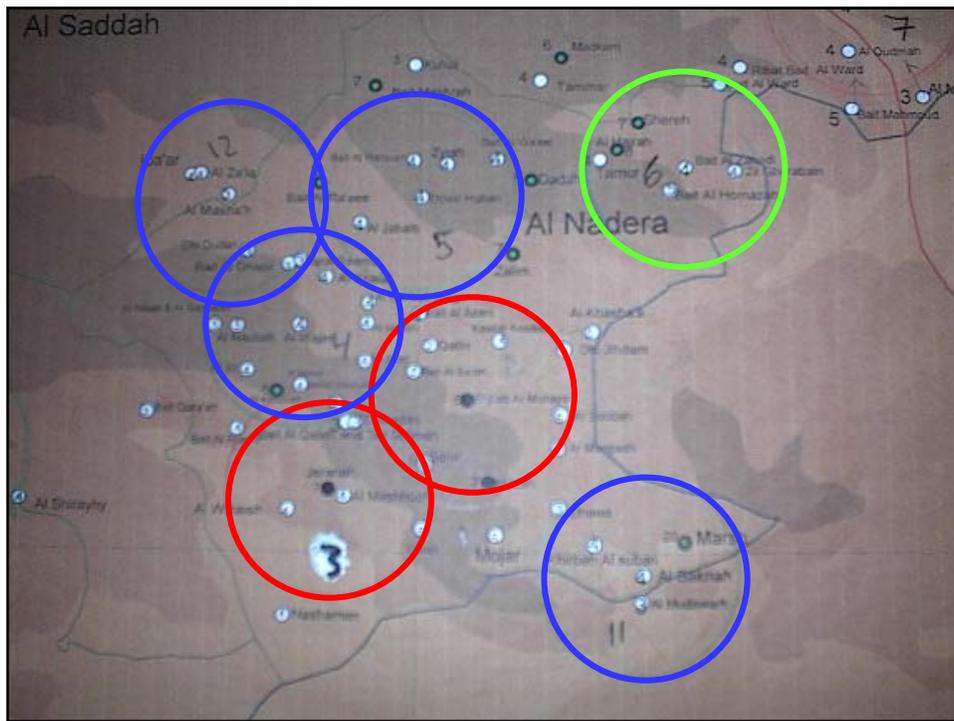










MRE IN

- communities / Villages / Fields / Schools
- distributing 5 Kind of brochures and posters (more then 350 000)
- broadcast in TV/Radio 8 sketches








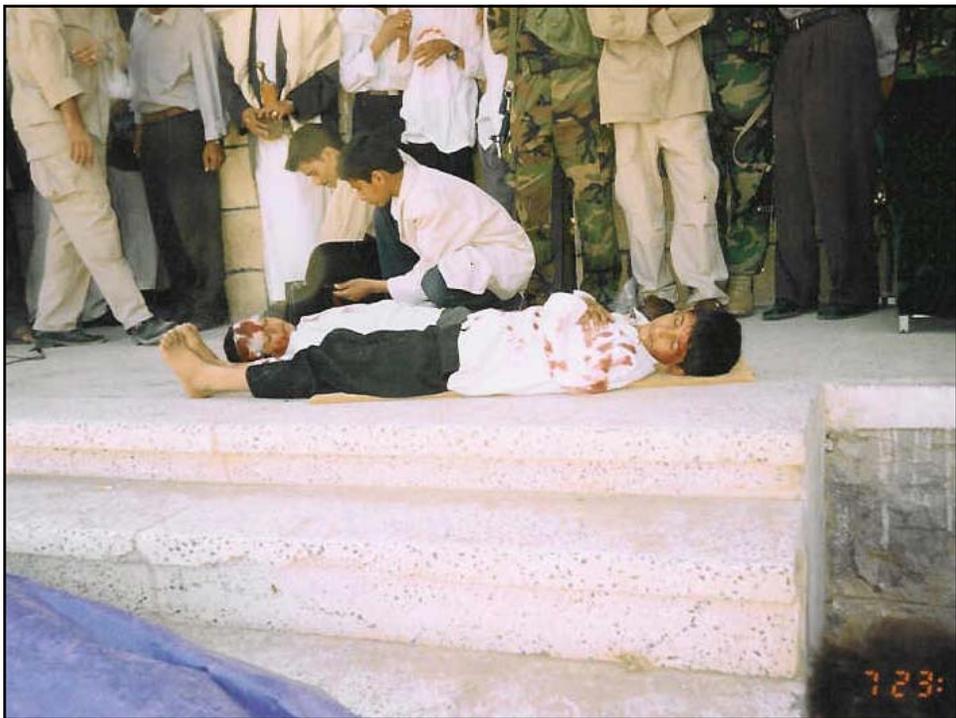















9. Mine Risk Education :
9.1 Summary :
9.2 Mine Risk Education By Months

| Year /Month | Men | Woman | Total | No. Vellages |
|---------------------|---------------|---------------|---------------|---------------------|
| 1999 | 0 | 0 | 0 | 0 |
| 2000 | 0 | 0 | 0 | 0 |
| 2001 | 24500 | 12000 | 36500 | 24 |
| 2002 | 141000 | 86000 | 227000 | 85 |
| 2003 | 38332 | 36648 | 74980 | 76 |
| 2004 | 52880 | 57960 | 110840 | 81 |
| Total | 256712 | 192608 | 449320 | 266 |
| 2005 | | | | |
| Jan. | 0 | 0 | 0 | 0 |
| Feb. | 140 | 167 | 307 | 6 |
| Mar | 1145 | 1535 | 2680 | 7 |
| Apr | 4210 | 4910 | 9120 | 6 |
| May | | | | |
| Jun | | | | |
| July | | | | |
| Aug | | | | |
| Sept | | | | |
| Oct | | | | |
| Nov | | | | |
| Dec | | | | |
| Total | 5495 | 6612 | 12107 | 19 |
| Ground Total | 262207 | 199220 | 461427 | 285 |

The difficulties, needs And *The* *Technical Challenges!*























Fuel Station Gas/Diesel



Motor Pool Dispatch



•Facilities


Motor Pool Covered Parking



Motor Pool Covered parking/Mech. Workshop



Ebinger 420GC

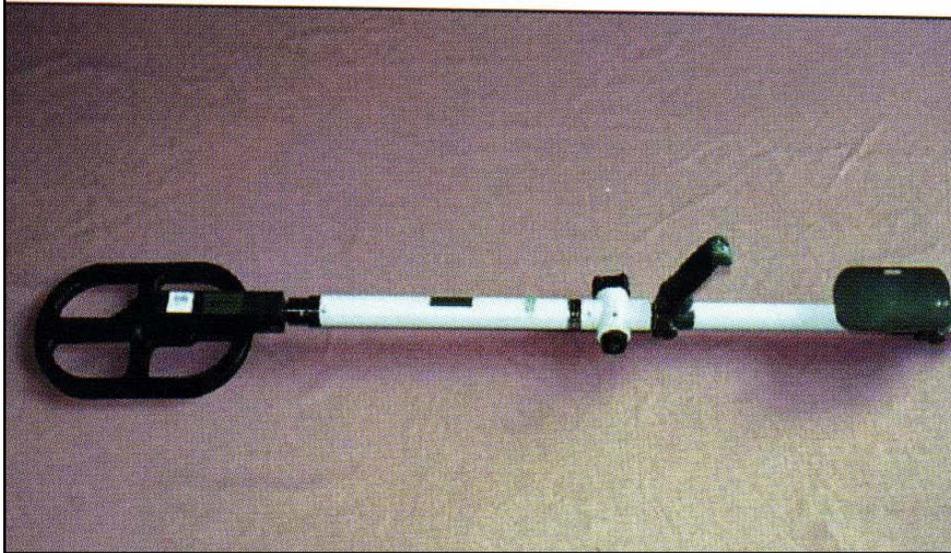

Yemen National Mine Action Programme



The Challenge!

- Eight clearance units (each 54 deminers, 27 demining pairs)
- Small-Minefields- to maintain 25 meter safety distance among pairs, a minefield must be 675 meters (27x25) wide to deploy an complete unit.
- YEMAC experience from the beginning of 2004 shows that one third of clearance force can't be deployed due to small size of MF
- Lower productivity- on average, a unit clear 15500 sqm/month
-

The solution

- 1- establish seven more survey teams
- 2- reconstruct tow Companies to six independent Platoons

* Without restructuring clearance Units and adding more survey teams Yemen will not be able to meet its obligation of the Ottawa Treaty set for March 2009.






The Achievements



3. Technical Survey:
Note: Reduced Area is area cleared out of mineField.
3.1 Area Marked by Year /Month :



| Year /Month | Marked Area | Reduced | Canceled | Total |
|---------------------|-------------------|----------------|--------------------|--------------------|
| 1999 | 108625 | 1200 | 5890175 | 6000000 |
| 2000 | 702122 | 61860 | 15876018 | 16640000 |
| 2001 | 1610665 | 97575 | 28146518.5 | 29854758.5 |
| 2002 | 4252623 | 97172 | 60084405 | 64434200 |
| 2003 | 2376572 | 32877 | 23343601 | 25753050 |
| 2004 | 2593407 | 18284 | 66729660 | 69341351 |
| Total | 11644014 | 308968 | 200070377.5 | 212023359.5 |
| 2005 | | | | |
| Jan. | 277648 | 14556 | 1869795 | 2161999 |
| Feb. | 161806 | 12568 | 3834426 | 4008800 |
| Mar | 316526 | 0 | -75775 | 240751 |
| Apr | 53920 | 0 | 0 | 0 |
| May | | | | |
| Jun | | | | |
| July | | | | |
| Aug | | | | |
| Sept | | | | |
| Oct | | | | |
| Nov | | | | |
| Dec | | | | |
| Total | 809900 | 27124 | 5628446 | 6411550 |
| Ground Total | 12,453,914 | 336,092 | 205,698,824 | 218,434,910 |

3.2 Marked Area by Governorates: (All Year)

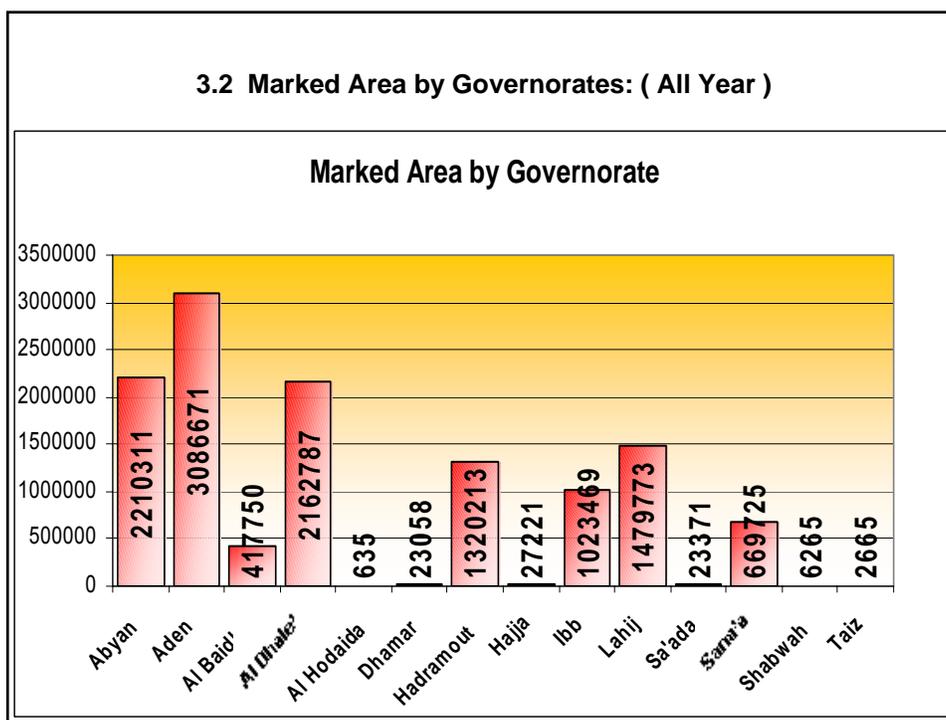

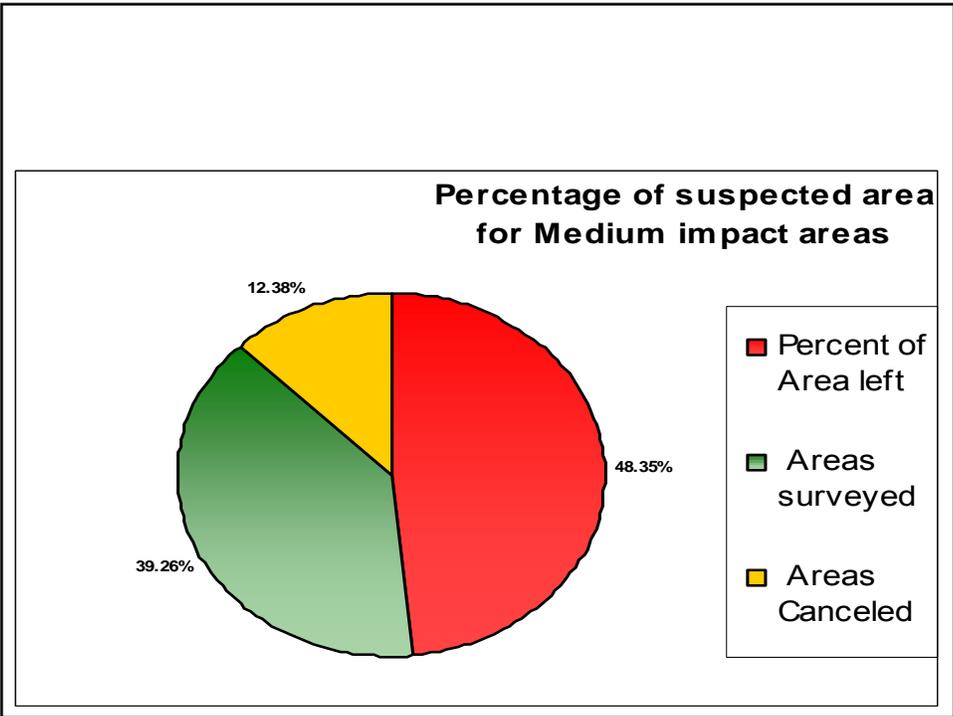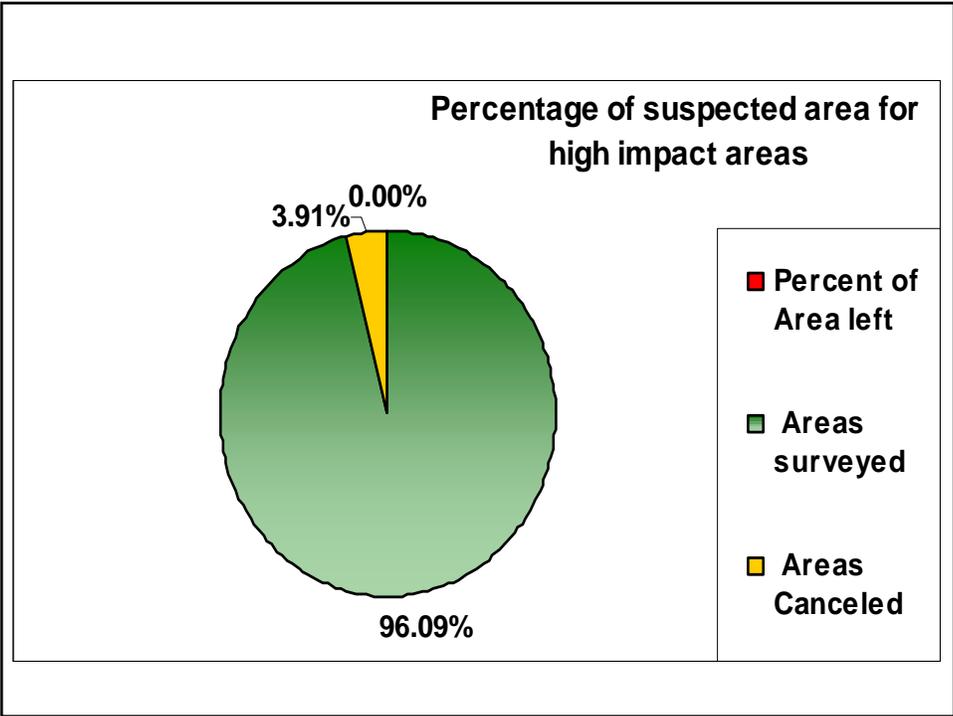


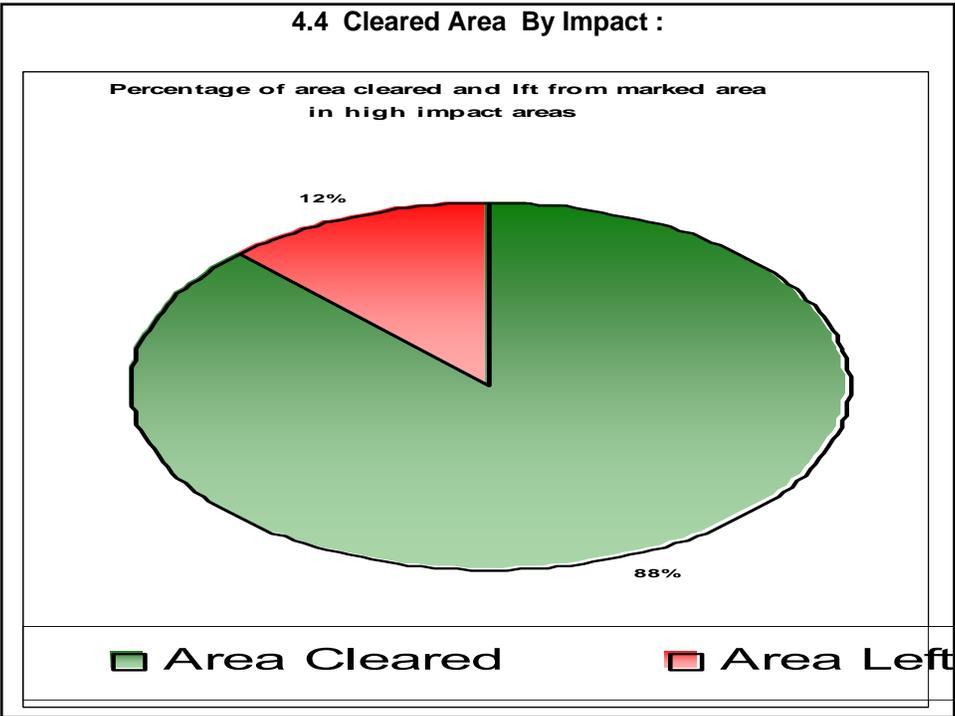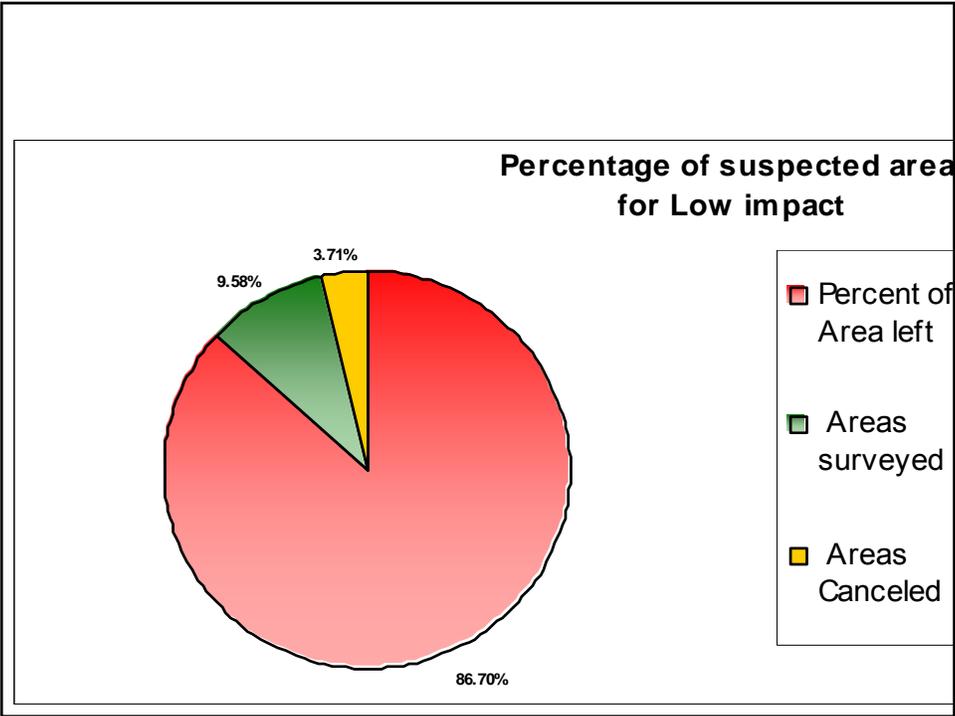

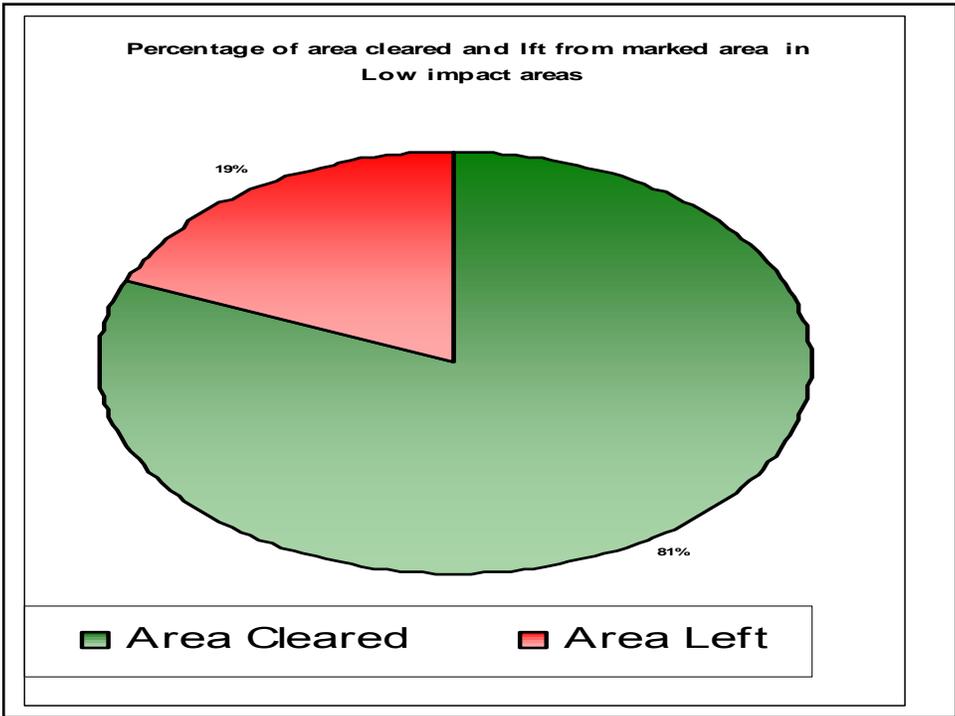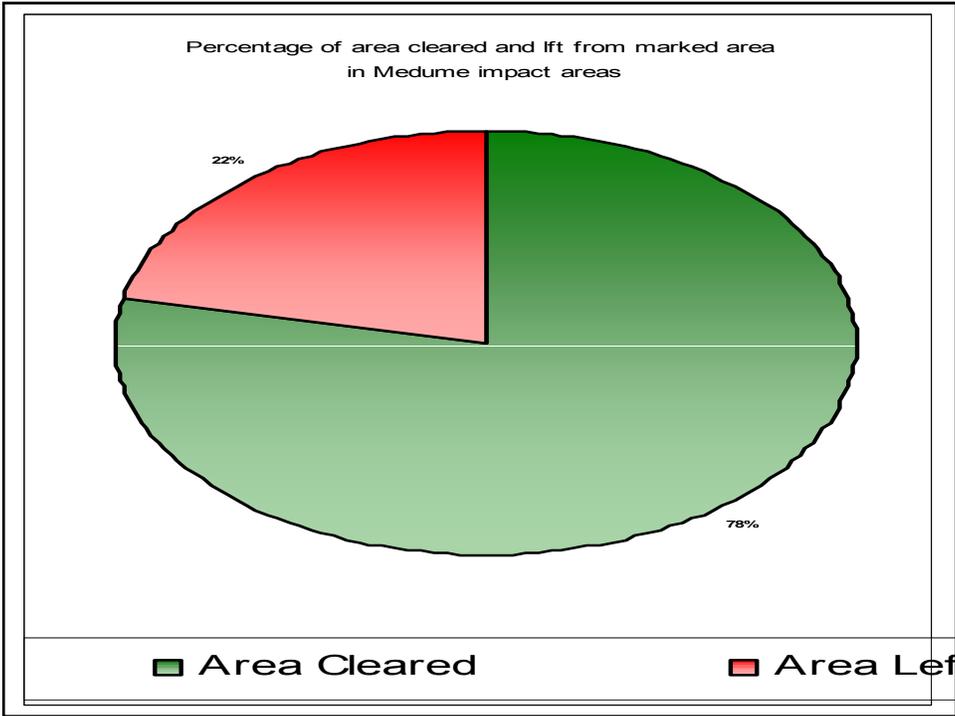

5. Devices Destroyed :

| Year /Month | AP | AT | UXO | Total |
|---------------------|--------------|------------|---------------|---------------|
| 1999 | 0 | 4 | 56305 | 56309 |
| 2000 | 5050 | 23 | 4897 | 9970 |
| 2001 | 4452 | 20 | 4369 | 8841 |
| 2002 | 68682 | 259 | 10961 | 79902 |
| 2003 | 91 | 38 | 15977 | 16106 |
| 2004 | 464 | 203 | 10594 | 11261 |
| Total | 78739 | 547 | 103103 | 182389 |
| 2005 | | | | |
| Jan. | 17 | 4 | 240 | 261 |
| Feb. | 1 | 4 | 59 | 64 |
| Mar | 3 | 6 | 814 | 823 |
| Apr | 14 | 5 | 517 | 536 |
| May | | | | |
| Jun | | | | |
| July | | | | |
| Aug | | | | |
| Sept | | | | |
| Oct | | | | |
| Nov | | | | |
| Dec | | | | |
| Total | 35 | 19 | 1630 | 1684 |
| Ground Total | 78774 | 566 | 104733 | 184073 |

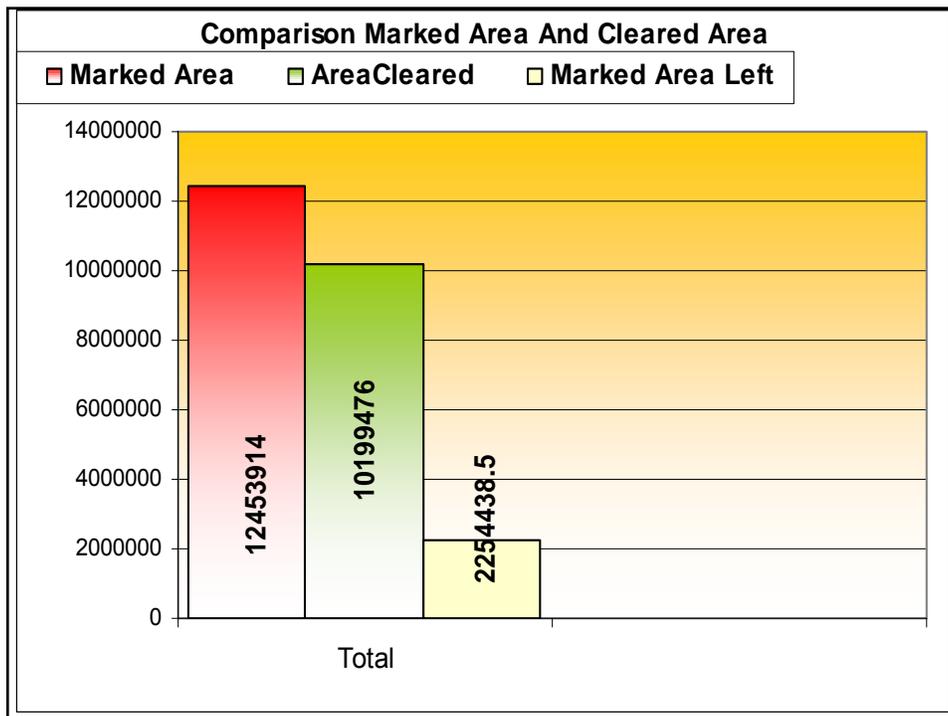

| No Mine Field Cleared (By Impact) : | | | | | |
|--------------------------------------|------------|-------------|-----------|-----------|--------------|
| Impact | No MF | MF Fenished | ongoing | MF Left | MF Suspended |
| High | 97 | 89 | 6 | 0 | 2 |
| Medium | 182 | 159 | 10 | 13 | 0 |
| Low | 109 | 74 | 14 | 19 | 2 |
| Total | 388 | 322 | 30 | 32 | 4 |

| Percentage of MinFields | |
|-------------------------|-----|
| MF Fenished | 83% |
| ongoing | 8% |
| MF Left | 8% |
| MF Suspended | 1% |
| | 0% |





Thank you

Mansour Al Ezzi

Project Manager UNDP
Director Of Yemen Executive Mine
Action Center

Email MANSAZI@y.net.ye

Phone 00 796 1302 790

00 796 73758242

Fax 00 1 796 302 791/5
