

TAJIKISTAN

PROGRESS ON IMPLEMENTATION OF EXTENSION REQUEST IN ACCORDANCE WITH ARTICLE 5 OF THE CONVENTION

11 Meetings of the States Parties to the Anti-Personnel Mine Ban


Phnom Penh, Cambodia, 28 November – 2 December 2011

1

CONTENT

1. **Introduction**
2. **Available capacity in 2011**
3. **Status of work to be conducted**
4. **Status of work conducted**
5. **Contaminated areas as of October 2012**
6. **Financial support in 2012**
7. **Operational plans for 2012**
8. **Other issues**

2

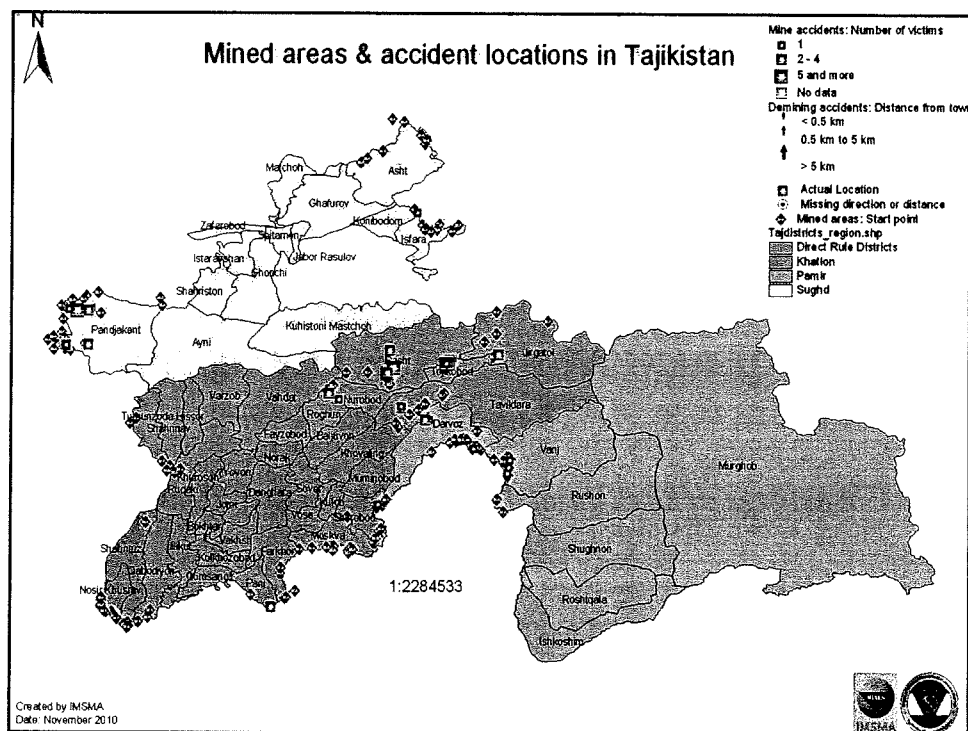

Available capacity in 2011

- ☐ 2 FSD Survey Teams
- ☐ 8 FSD Multipurpose Teams
- ☐ 6 MDD Teams (12 dogs) – Managed by FSD
- ☐ 2 FSD mechanical demining teams (2 MV-4 machines)
- ☐ 1 MoD mechanical demining team (1 Mini MineWolf)
- ☐ 4 NPA Multipurpose Teams
- ☐ Establishing new NPA MDC with 5 MDD Teams (10 dogs)

Status of work to be conducted

Assumptions for 2011 in accordance with Work Plan of Extension Request

	Land release by	Number of areas to be cleared or reduced	Size to be cleared or reduced, m ²
Tajik Afghan border	MDM	21	700,000
	MDD	7	400,000
	Manual	1	200,000
Central Region	MDM	4	500,000
	Manual	2	100,000
		35	1,900,000

5

Status of work conducted

Progress made in 2011

	Land released by	Number of cleared (prepared) areas	Number of ongoing areas	Cleared (prepared) size, m ²
Tajik Afghan border	MDM area preparation	(16)	(1)	(967 500)
	MDD	5	2	149 000
	Manual	11	4	800 000
	Mixed (MDD and manual)	10	-	471 000
Central Region	MDM area preparation	(2)	-	(190 500)
	Mixed (Follow up)	2 (not completed)	-	180 000
		26	7	1 600 000

6

Status of work to be conducted

Assumptions for 2012 in accordance with Work Plan of Extension Request

	Land release by	Number of areas to be cleared or reduced	Size to be cleared or reduced, m ²
Tajik Afghan border	MDM		0
	MDD	17	400,000
	Manual	9	200,000
Central Region	MDM	1	200,000
	Manual	1	100,000
		28	900,000

7

Plan for 2012

In accordance with Long Term Action Plan 2012-2015 (Strategic Plan 2010-2015)

	Land release, m2		Mechanical demining operations, m2			Total Land release, m2
	Manually	Mine detection Dogs	Total Ground Preparation	Follow up manually	Follow up by MDDs	
2012	200,000	100,000	1,000,000	100,000	900,000	1,300,000

- Initial Survey on military polygons
- BAC operations in Central Region
- Resurvey operations

8

Contaminated areas as of October 2011

Total size of contaminated and leftover areas:

- **Tajik-Afghan Border:** 177 areas – 6,7 km²
- **Central region:** 26 areas - 2,3 km²
- **Tajik-Uzbek border:** 57 areas – survey started

9

Financial support in 2011

Canada	UNDP
Germany	OSCE
Japan	ICRC
Norway	
USA	
Australia	

10

Other issues

- TMAC Nationalization
- Contribution of Government
- MRE activities
- VA activities
- Tajik – Uzbek border

11

Thank you for your attention

12

TAJIKISTAN

PROGRESS ON IMPLEMENTATION OF EXTENSION REQUEST IN ACCORDANCE WITH ARTICLE 5 OF THE CONVENTION

11 Meetings of the States Parties to the Anti-Personnel Mine Ban


Phnom Penh, Cambodia, 28 November – 2 December 2011

1

CONTENT

1. Introduction
2. Available capacity in 2011
3. Status of work to be conducted
4. Status of work conducted
5. Contaminated areas as of October 2012
6. Financial support in 2012
7. Operational plans for 2012
8. Other issues

2

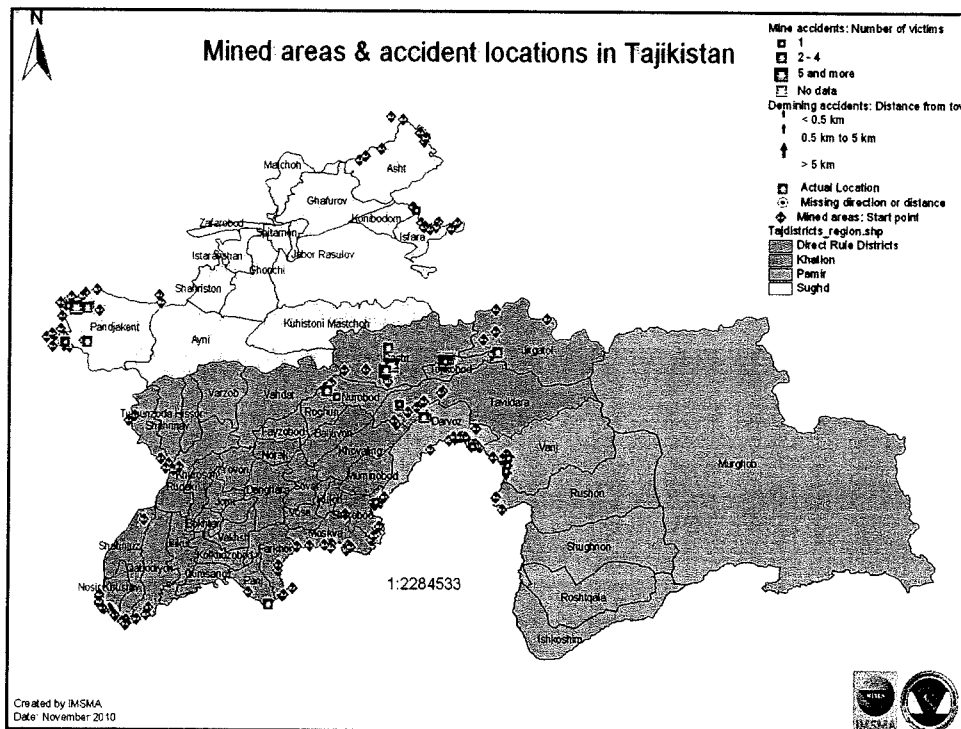

Available capacity in 2011

- ❑ 2 FSD Survey Teams
- ❑ 8 FSD Multipurpose Teams
- ❑ 6 MDD Teams (12 dogs) – Managed by FSD
- ❑ 2 FSD mechanical demining teams (2 MV-4 machines)
- ❑ 1 MoD mechanical demining team (1 Mini MineWolf)
- ❑ 4 NPA Multipurpose Teams
- ❑ Establishing new NPA MDC with 5 MDD Teams (10 dogs)

Status of work to be conducted

Assumptions for 2011 in accordance with Work Plan of Extension Request

	Land release by	Number of areas to be cleared or reduced	Size to be cleared or reduced, m ²
Tajik Afghan border	MDM	21	700,000
	MDD	7	400,000
	Manual	1	200,000
Central Region	MDM	4	500,000
	Manual	2	100,000
		35	1,900,000

5

Status of work conducted

Progress made in 2011

	Land released by	Number of cleared (prepared) areas	Number of ongoing areas	Cleared (prepared) size, m ²
Tajik Afghan border	MDM area preparation	(16)	(1)	(967 500)
	MDD	5	2	149 000
	Manual	11	4	800 000
	Mixed (MDD and manual)	10	-	471 000
Central Region	MDM area preparation	(2)	-	(190 500)
	Mixed (Follow up)	2 (not completed)	-	180 000
		26	7	1 600 000

6

Status of work to be conducted

Assumptions for 2012 in accordance with Work Plan of Extension Request

	Land release by	Number of areas to be cleared or reduced	Size to be cleared or reduced, m ²
Tajik Afghan border	MDM		0
	MDD	17	400,000
	Manual	9	200,000
Central Region	MDM	1	200,000
	Manual	1	100,000
		28	900,000

7

Plan for 2012

In accordance with Long Term Action Plan 2012-2015 (Strategic Plan 2010-2015)

	Land release, m2		Mechanical demining operations, m2			Total Land release, m2
	Manually	Mine detection Dogs	Total Ground Preparation	Follow up manually	Follow up by MDDs	
2012	200,000	100,000	1,000,000	100,000	900,000	1,300,000

- Initial Survey on military polygons
- BAC operations in Central Region
- Resurvey operations

8

Contaminated areas as of October 2011

Total size of contaminated and leftover areas:

- ❑ **Tajik-Afghan Border:** 177 areas – 6,7 km²
- ❑ **Central region:** 26 areas - 2,3 km²
- ❑ **Tajik-Uzbek border:** 57 areas – survey started

9

Financial support in 2011

Canada	UNDP
Germany	OSCE
Japan	ICRC
Norway	
USA	
Australia	

10

Other issues

- TMAC Nationalization
- Contribution of Government
- MRE activities
- VA activities
- Tajik – Uzbek border

11

Thank you for your attention

12
