




Mine-free after 2025
Tajikistan Article 5 Extension Request

Presented by Mr. Muhabbat Ibrohimzoda
Director Of Tajikistan National Mine Action Center

Achievements during the previous extension period (2010-2018)

Diagram 1: Summary areas released in million square meters (2009 – 2018)

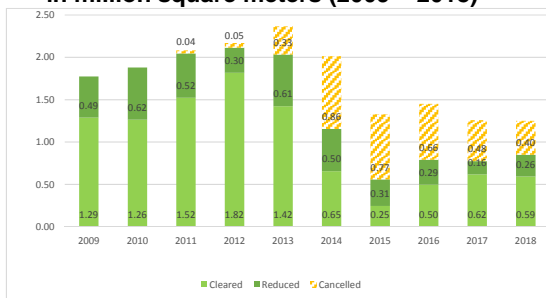

2010 Remaining challenge: **14,849,631m²**

Target for the period 2009-2019:
14,860,000m².

Tajikistan addressed **17,565,639m²** for the period 2009-2018 representing progress of (124%) against the target.

7 districts declared 'mine-free'.

During 2010-2018, previously unknown mined areas measuring **10,485,815 m²** were identified.

The highest rates of released land performed in the period 2010-2014 as a result of deployed mechanical demining assets in the flat areas of Tajik-Afghan border.



Landmines & UXO Destroyed

77,846



Land cleared and reduced

13,973,190 sqm





Land cancelled by non-technical survey

3,592,449 sqm



Total land released and handed over

17,565,639 sqm

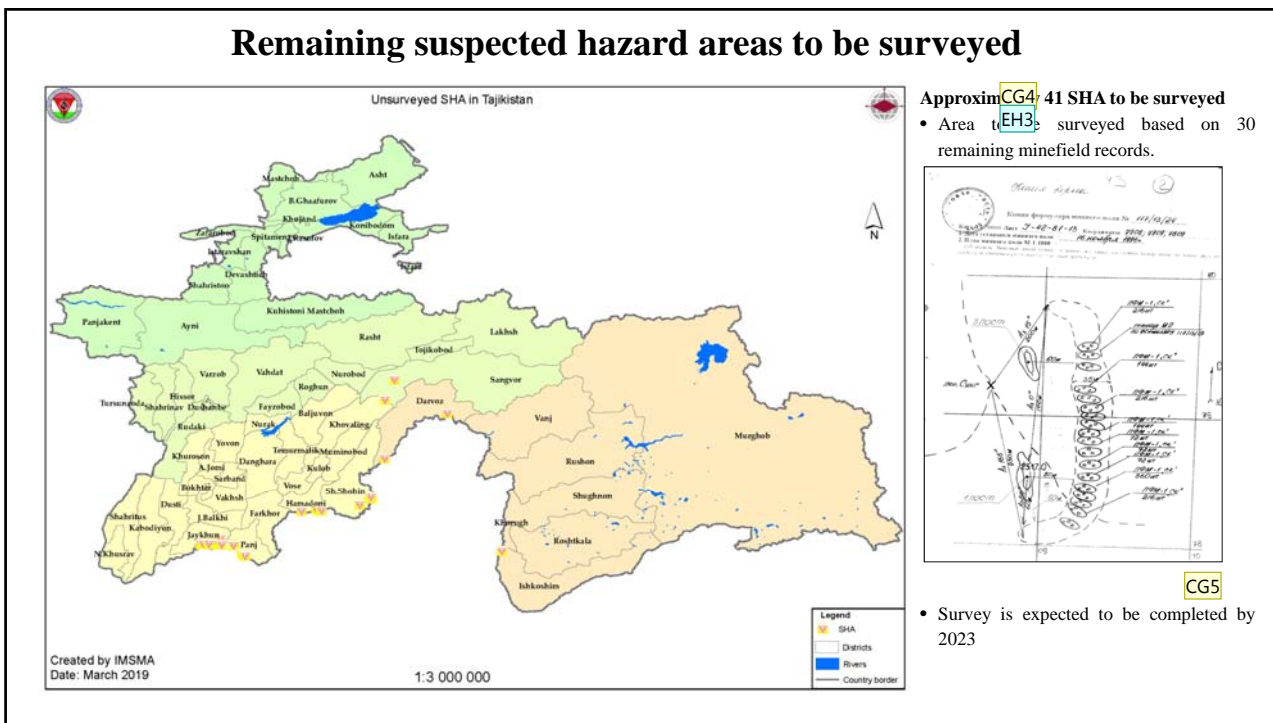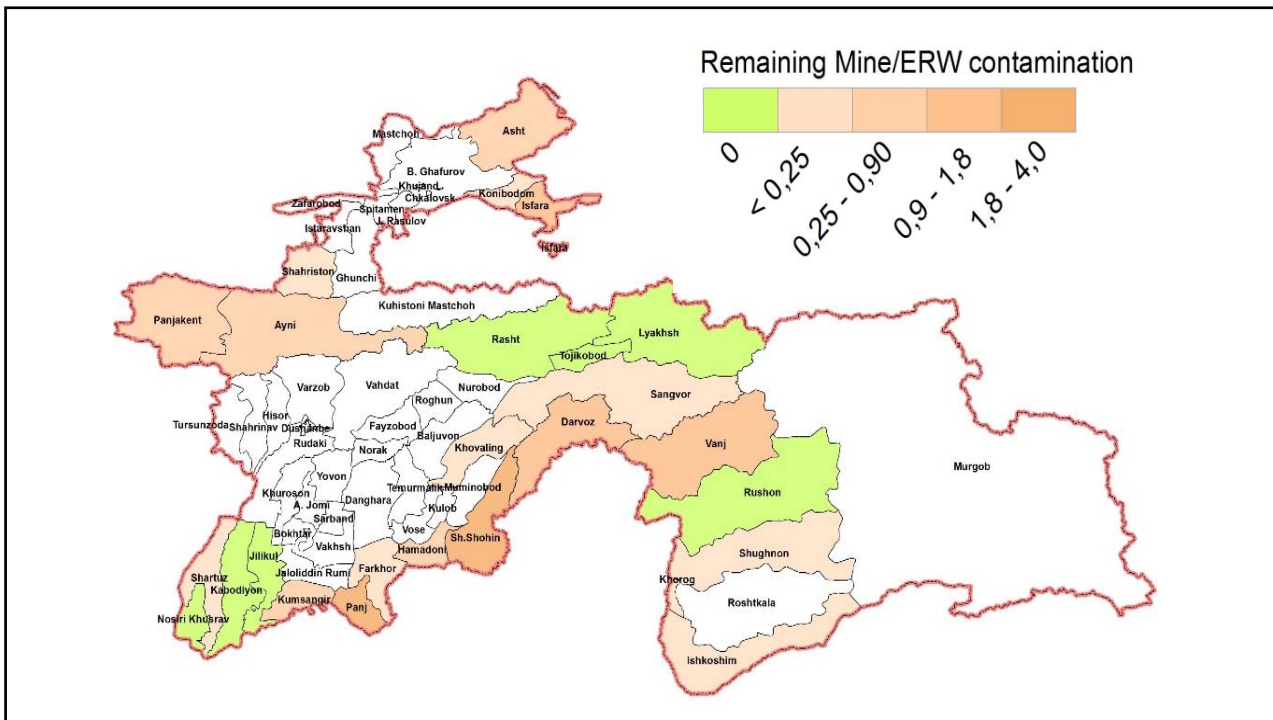

Slide 4

CG4 Is this correct?

Cathcart Gregory; 12.03.2019

EH3 yes we 30 MFR where 41 Suspected hazard areas

Erkin Huseinov; 12.04.2019

CG5 Please give some updated timeline for completion

Cathcart Gregory; 12.03.2019

Plan to address remaining contamination

Tajikistan has a remaining challenge of 249 hazardous areas measuring 12,098,210m².


This includes:

- 154 confirmed hazardous areas measuring 7,907,210m²
- 41 SHA measuring an estimated 941,000m².
- 54 SHA measuring 3,250,000m² (Tajik –Uzbek border)


During the extension period Tajikistan will address the following:

- 195 CHA&SHA measuring 8,848,210 m²
- This target excludes 54 SHA measuring 3,250,000m² on the Tajik-Uzbek border, that will be addressed once a political agreement has been made.

This 2025 goal is based on doubling current capacity.



Clearance rate projection based on capacity available in 2019

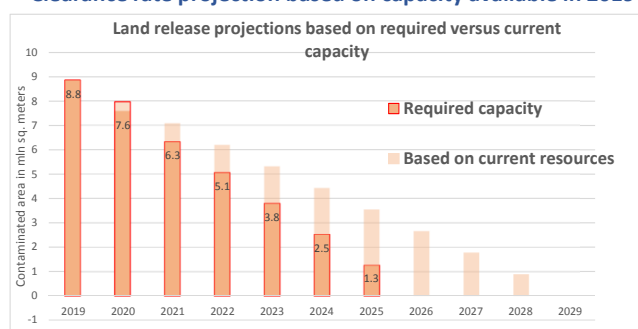

Current cooperation and assistance and challenges

Year	Annual Milestone (square metres)	Current national resources (US \$)	Current international resources (US \$)	Additional Funding Required for increasing capacity	Total
2020	1 388 819	480 000	2 600 000	3 400 000	6 480 000
2021	1 218 722	480 000	2 600 000	1 800 000	4 880 000
2022	1 284 655	480 000	2 600 000	1 800 000	4 880 000
2023	1 277 666	480 000	2 600 000	1 800 000	4 880 000
2024	1 138 919	480 000	2 600 000	1 800 000	4 880 000
2025	1 170 000	480 000	2 600 000	1 800 000	4 880 000
TOTAL	7 478 781	2 880 000	15 600 000	12 400 000	30 880 000

Challenges and Needs

Challenges	Needs
<ul style="list-style-type: none"> Funding required to double capacity to meet extension target 	<ul style="list-style-type: none"> Equipment: Vehicles and demining equipment (PPE, detectors, uniforms, etc.) for 10 new teams Old vehicles, detectors, visors, office equipment need replacing
<ul style="list-style-type: none"> Security situation: Situation on Tajik / Afghan border sensitive, and changes quickly. 	<ul style="list-style-type: none"> Security: Additional support from Border Guards
<ul style="list-style-type: none"> There are still 41 un-surveyed areas measuring 941 000 m², which will be surveyed until 2023 and released up to 2025 	<ul style="list-style-type: none"> Funding: Additional 12,400,000 USD over 5 years (Total 30,830,000)
<ul style="list-style-type: none"> Short demining season: Rain, snow and hot weather restricts operational time. In some mountainous areas the climate only allows 40 operational days per year Access to remote terrain; slope and altitude - harder to operate 	<ul style="list-style-type: none"> Assistance to continue for NTS with technical intervention (survey)

