# PERÚ APMBC INTERSESSIONAL MEETING

REQUEST OF RENEW EXTENSION DEADLINE ACCORDING TO ARTICLE 5 GENEVA, MAY 19, 2016

#### SITUATION OF THE REQUEST – DEADLINE MARCH 1ST, 2017

- In april 2008, Perú requested an extenssion of its deadline for completing the destruction of all anti-personnel mines
- 362,232 m2 affected with landmines
- 190,000 m2 in Cordillera del Cóndor, in the border with Ecuador.
- 35 dangerous areas became 38.
- 2016: will conclude 6 remnants dangerous areas from the initial request: Portero 09, Betty, Mirador 02, Mirador 2\_06, Cunhuime 03 y CG 89.

#### EXCHANGE OF INFORMATION WITH ECUADOR

- Perú recognices the importance of cooperation and assistance with Ecuador.
- Both countries adopted several confident building measures in mine action, one of them Mine Action National Authorities Meetings and, throught this mechanism, the exchange of information about dangerous areas.
- Perú started this process of exchange of information with Ecuador in May 2010, during the IV Meeting of Mine Action National Authorities, with the delivery of information about 13 dangerous areas in Ecuadorian soil.

#### EXCHANGE OF INFORMATION WITH ECUADOR

- Between November 2012 and December 2013, Ecuador provided information about 128 dangerous areas in Peruvian soil.
- In march 2015, Ecuador provided to Perú information about 10 dangerous areas in Peruvian soil, within an Ecuadorian private property area (Km2 in Tiwinza), according to Brasilia Peace Agreements of 1998. Both countries agree to task "Perú-Ecuador Binational Unit of Humanitarian Demining" to implement clearance on these areas.

#### REASONS FOR THE NEW REQUEST

- Volume of information received (138 dangerous areas)
- Geographical scattering of these new areas
- 411,694 m2 affected with landmines in Cordillera del Cóndor
- Comparing 2008 request, this new situation constitutes a bigger area and located totally in the mountainous jungle.
- This means: new challenge

Mountainous jungle over 3,000 msmn




- Mountainous jungle over 3,000 msmn
- Inusual and frequent rains



- Mountainous jungle over 3,000 msmn
- Inusual and frequent rains
- No roads



- Mountainous jungle over 3,000 msmn
- Inusual and frequent rains
- No roads
- Long way between I up to 3 hours to arrive to the operational area

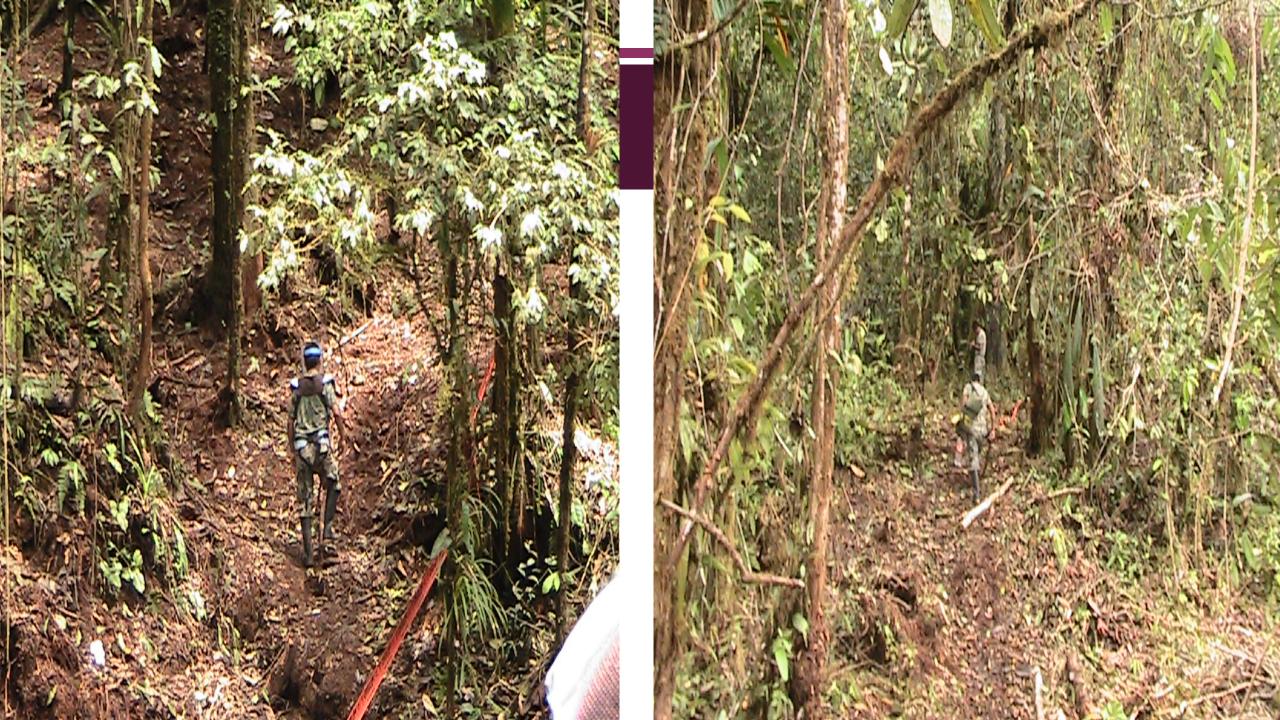




- Mountainous jungle over 3,000 msmn
- Inusual and frequent rains
- No roads
- Long way between I up to 3 hours to arrive to the operational area
- Lack of medical infrastructure or hospitals nearby

# THE REQUEST

- Since March 2, 2017: 128 dangerous areas
- 411,694 m2
- 6,338 landmines
- Until December 31, 2025

# **PROGRAMMME 2017-2025**

N/O	SECTORS	2017	2018	2019	2020	2021	2022	2023	2024	2025	TOTAL		
		8 Jor.	ССММ	MINAS	ÁREA m2								
1	SANTIAGO				07	08	08	09	08	04	44	2,974	76,290
2	TIWINZA	10	08	08							26	1,573	132,680
3	CENEPA		06	05	07	07	06	05			36	1,399	21,759
4	ACHUIME								10	08	18	392	180,965
	TOTAL	14	14	13	14	15	14	14	18	12	128	6,338	411,694

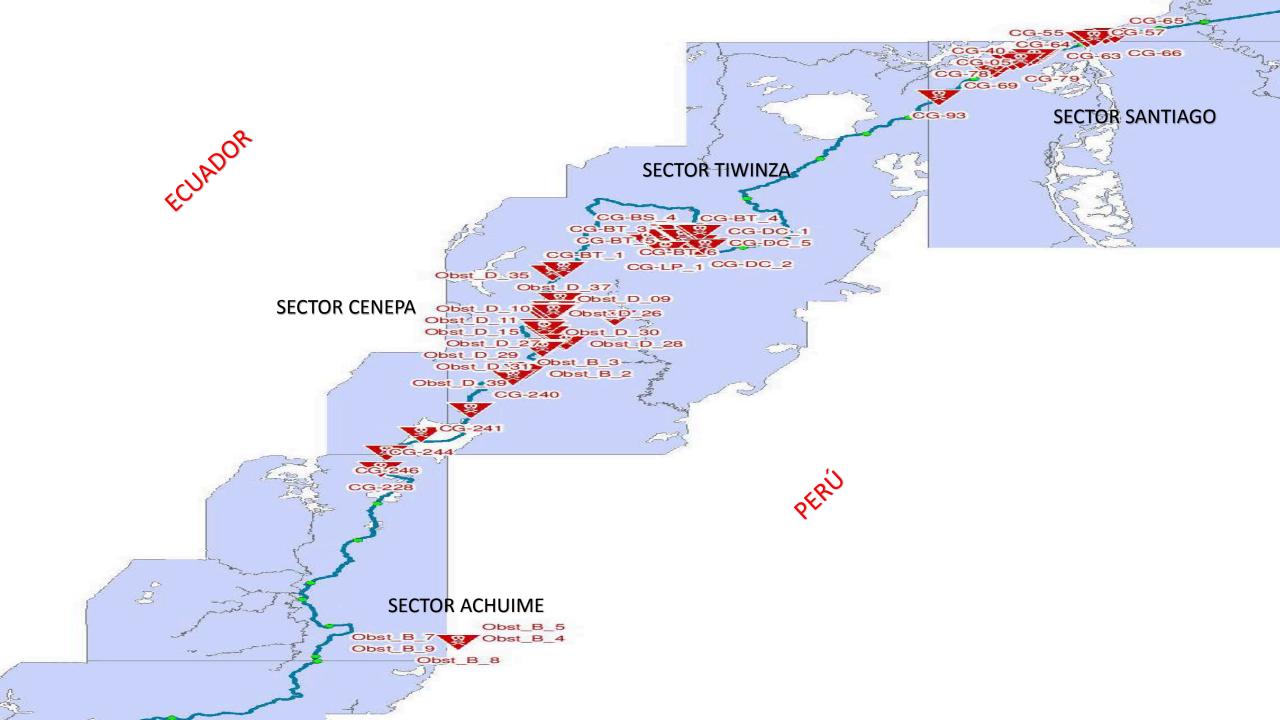

# BUDGET

- US\$ 39'073,673 aproximately
- Funded by Peruvian Government

#### INTERNATIONAL COOPERATION

- Could join us to implement faster than we scheduled (December 2025)
- Implementation of new techniques in clearance operations (rats, new technology, others)
- Strengthening of the Demining School
- Life insurances for the deminers
- Equipment in general: detectors, personal protection equipment (PPE), solar panels, tents.

#### PREPARATION OF THE REQUEST

- Ad hoc Working Group for the ellaboration of these 3 documents:
- Integral National Plan in Mine Action 2017-2025; Humanitarian Demining National Plan 2017-2025; and the new request.
- Executive Council of CONTRAMINAS approved these documents on March 29, 2016
- Peru request a new extension on March 30, 2016 in Geneva.
- http://www.apminebanconvention.org/fileadmin/APMBC/clearing-mined-areas/art5\_extensions/countries/Peru-ExtRequest-Received-30Mar2016-sp.pdf

